

PulseCheck School Onboarding Instruction Manual

Visual admin guide with real Playwright screenshots from the live local PulseCheck app.

Prepared for	PulseCheck implementation admins and launch staff
Document status	Visual review draft - June 5, 2026
Screenshot source	Playwright captures from localhost PulseCheck admin screens using saved admin storage state

Manual purpose

Use this as the standard operating guide for onboarding a new school. The screenshots show where admins work in the product; the team tracker remains the live source of truth.

1. Route Map And Status Legend

Admins should not need to memorize process language. Use the route map to find the right screen, then use the four visual status labels below to keep each team launch moving.

Screen	Route	Used for
Onboarding Playbook	/admin/pulsecheckOnboardingOverview	Review rollout sequence, launch-ready definition, and templates.
Provisioning Console	/admin/pulsecheckProvisioning	Create and review organizations, teams, pilots, cohorts, support routes, and invite links.
Team Tracker	Expanded team card in provisioning	Monitor school launch status without leaving the provisioning console.
Launch-Day Mode	Team workspace with mode=launch-day	Run athlete invite, setup, device sync, check-in, and first protocol or simulation flow.

Status at a glance

Not started No action yet	Working Owner is handling it
Done Verified and ready	Needs help Escalate before launch

Simple rule


Only mark a step Done when it is verified. If the next meeting or launch day is at risk, mark it Needs help and assign an owner.

2. Operating Model

PulseCheck school onboarding is a three-meeting deployment with pre-work and post-launch monitoring. The admin provisions the school, the coach is trained before athletes arrive, and team launch is managed as a room flow.

Phase	Owner	Done when
0. Intake	PulseCheck admin	Sponsor, staff list, roster estimate, launch window, support route, and device plan are confirmed.
1. Provision	PulseCheck admin	Organization, team, pilot or cohort, commercial posture, support route, and invite paths are configured.
2. Coach kickoff	PulseCheck staff	Coach understands rollout goals, data boundaries, support contacts, device plan, and next actions.
3. Dashboard training	PulseCheck staff	Coach can read Nora reports, use follow-up, and avoid over-reading thin data.
4. Team launch	PulseCheck staff + coach	Athletes join the app, sync devices, complete setup, learn check-ins, and complete first protocol or simulation.
5. Monitor	PulseCheck staff + coach	Coach receives snapshots, blockers are tracked, and stakeholders meet every two weeks.

3. Admin Playbook Screen

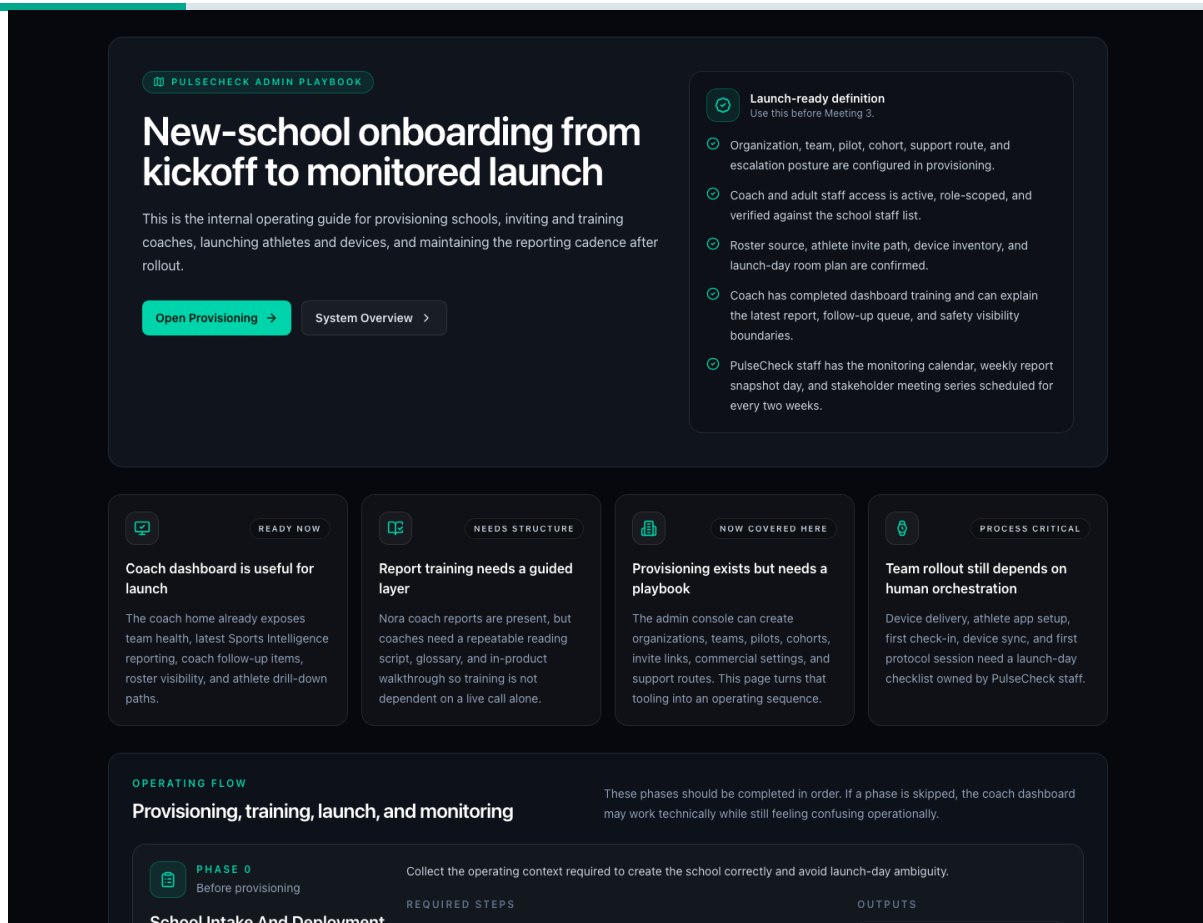


Screenshot 1 - Admin onboarding playbook overview.

Use this page first. It gives the launch-ready definition, process checkpoints, operating flow, and links into Provisioning and System Overview.

Use this screen to

- Review the full school rollout before creating new records.
- Confirm the three-meeting flow with PulseCheck staff.
- Open Provisioning when the school is ready to create or review.

4. Provision The School

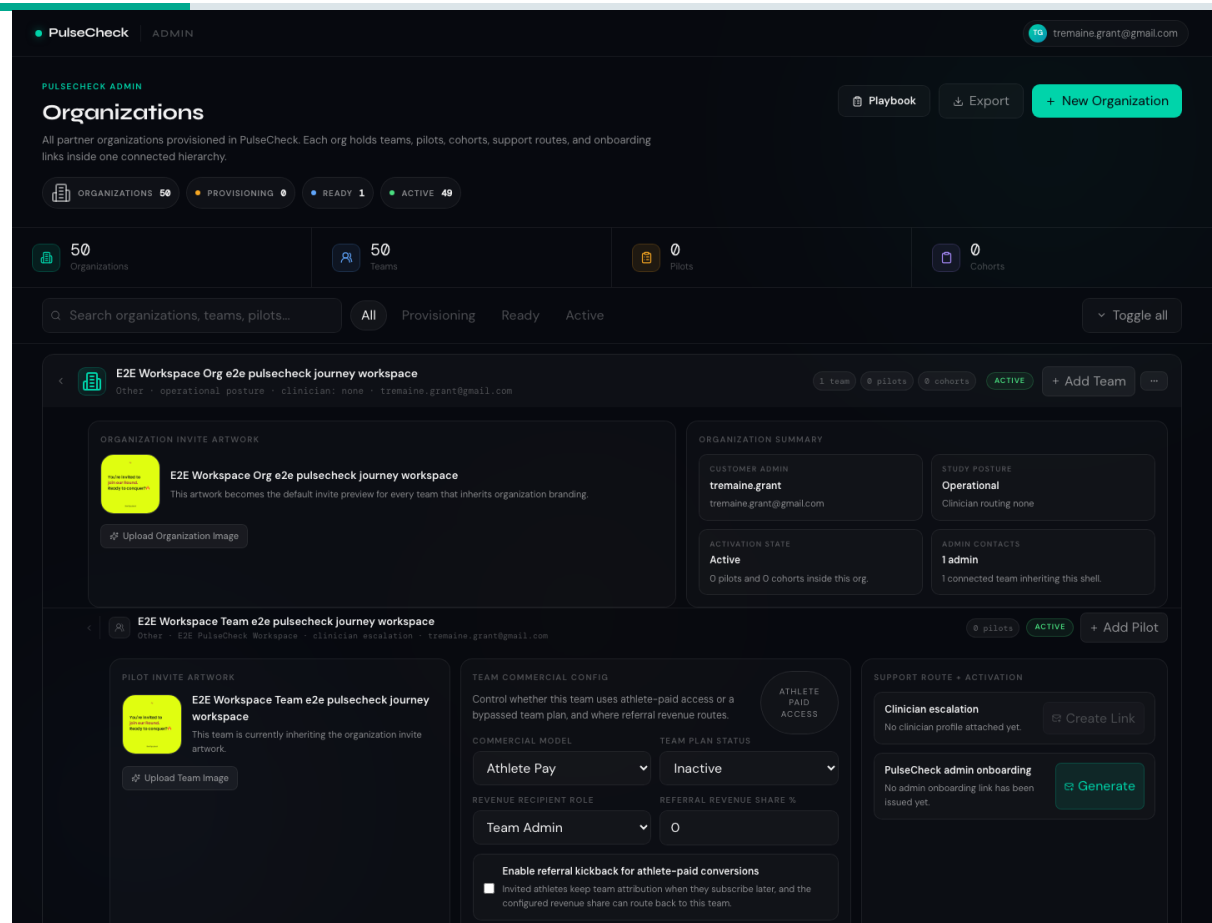

Screenshot 2 - PulseCheck provisioning console overview.

This is the admin control surface for organizations, teams, pilots, cohorts, invite links, support routing, commercial posture, and onboarding tracker access.

Provisioning sequence

- Create the organization with school display name, legal name, organization type, customer admin, and study posture.
- Create the operating team with sport, season label, team status, plan status, commercial model, roster policy, and escalation route.
- Create pilot and cohort records when the deployment is part of a pilot, study, or phased rollout.
- Generate admin activation and coach invite paths only after role and team routing are verified.
- Review support contacts, clinician bridge mode, team preview assets, commercial configuration, and invite policy.

5. Team Onboarding Tracker

TEAM ONBOARDING TRACKER

E2E Workspace Team e2e pulsecheck journey workspace launch readiness

Track the full school rollout from intake through weekly coach snapshots and stakeholder check-ins. Status changes save to this team record.

0 of 10 steps complete No steps need help

NOT STARTED No action yet **WORKING** Owner is handling it **DONE** Verified and ready **NEEDS HELP** Escalate before launch

School intake complete Before kickoff - PulseCheck admin School sponsor, coach list, roster estimate, launch window, support route, and device plan are confirmed. NOT STARTED Not started	Org and team provisioned Before kickoff - PulseCheck admin Organization, team, pilot posture, cohort plan, commercial settings, and invite policies are configured. NOT STARTED Not started
Meeting 1 kickoff complete Meeting 1 - PulseCheck staff Coach understands rollout goals, roles, data boundaries, device plan, and next actions. NOT STARTED Not started	Meeting 2 dashboard training complete Meeting 2 - PulseCheck staff Coach can read Nora reports, use the dashboard, review follow-up, and avoid over-reading thin data. NOT STARTED Not started
Meeting 3 team launch scheduled Meeting 3 - PulseCheck admin Team room plan, invite flow, delivery support, troubleshooting lane, and athlete training agenda are ready. NOT STARTED Not started	Devices delivered and synced Launch day - PulseCheck staff Device inventory is reconciled and athlete source status is healthy or logged for follow-up. NOT STARTED Not started
First team check-in complete Launch day - Coach + athletes Athletes complete the first check-in and understand when honest daily input is expected. NOT STARTED Not started	First protocol or simulation complete Launch day - Coach + athletes Athletes complete the first assigned mental training experience with PulseCheck staff present. NOT STARTED Not started
Weekly coach snapshot cadence active Post-launch - Coach success PulseCheck staff has the weekly report snapshot day, owner, and coach delivery path confirmed. NOT STARTED Not started	Stakeholder check-ins scheduled Post-launch - PulseCheck lead Coach and stakeholder check-ins are scheduled every two weeks with agenda owner and action log. NOT STARTED Not started

Screenshot 3 - Team onboarding tracker with visual status legend.

The tracker is intentionally simple: one progress bar, four status labels, and one dropdown per launch step.

Tracker steps to update

- School intake complete.
- Organization and team provisioned.
- Meeting 1 kickoff complete.
- Meeting 2 dashboard training complete.
- Meeting 3 team launch scheduled.
- Devices delivered and synced.
- First team check-in complete.
- First protocol or simulation complete.
- Weekly coach snapshot cadence active.
- Every-two-weeks stakeholder cadence active.

6. Coach Kickoff And Dashboard Training

Meeting 1 is a soft training session. Meeting 2 is the hands-on dashboard training session. Keep both simple: the coach needs to understand the rollout, where reports live, how to read Nora, and what not to over-read.

Meeting 1 coach kickoff

- Confirm deployment goal, launch date, team scope, and first-month learning goal.
- Review PulseCheck roles, school roles, support contacts, and escalation boundaries.
- Preview the coach dashboard, Nora coach reports, daily check-ins, mental training, device delivery, and the next two meetings.
- Confirm staff list, roster estimate, device plan, and dashboard training date.


Meeting 2 dashboard training

- Open `/coach/dashboard?training=1` with a coach account.
- Start with the latest Sports Intelligence report.
- Review team snapshot, meaningful shifts, adherence coverage, athlete flags, coach actions, and data limitations.
- Use coach follow-up as a queue, not a crisis list.
- Open report archive only after the latest report is understood.

Training standard

Do not act on one thin signal without checking coverage, trend direction, and context. The report supports decisions; it does not replace judgment.

7. Admin Templates

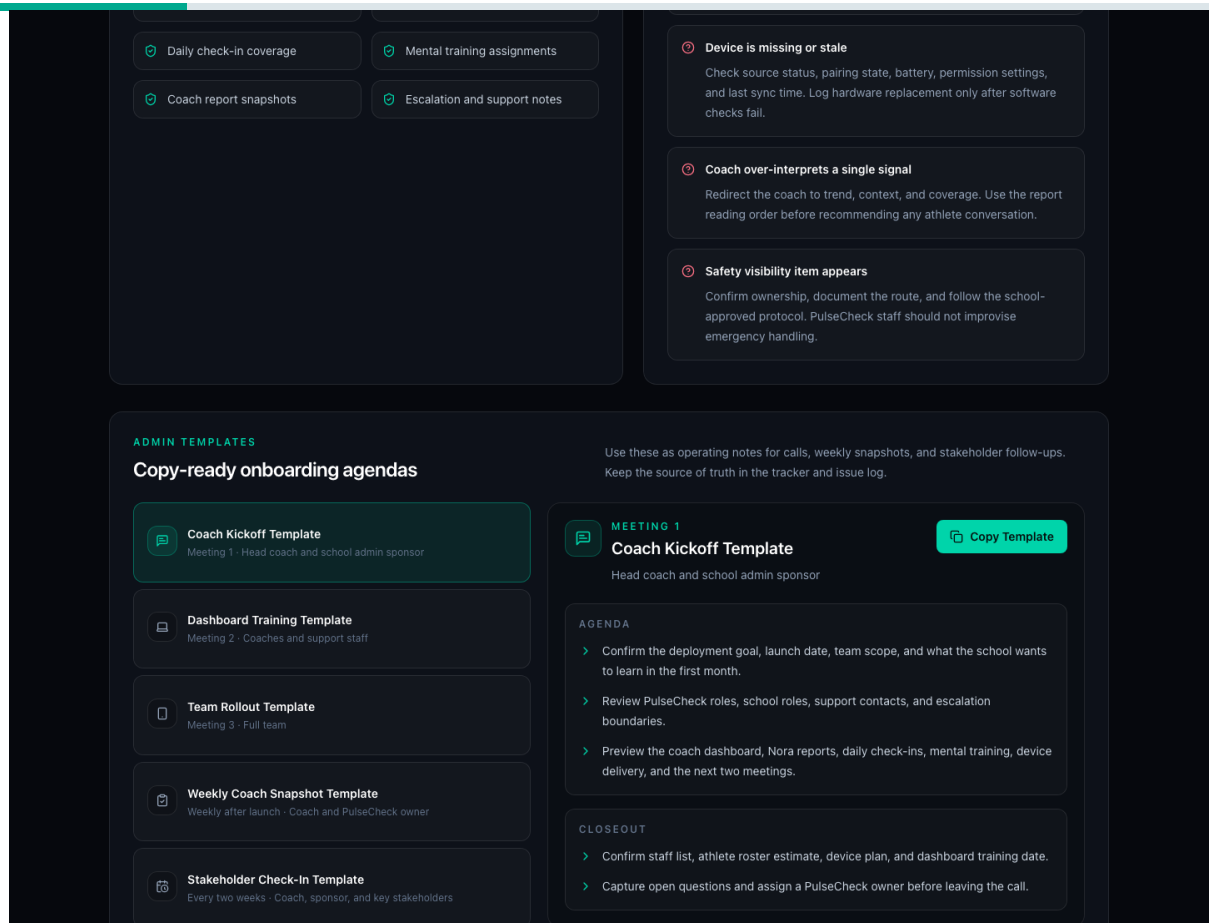


Screenshot 4 - Copy-ready onboarding templates.

Use the templates during calls and weekly follow-up. Copy the active template and adapt it to the school while keeping the tracker as the source of truth.

Template usage

- Coach Kickoff Template: use before and during Meeting 1.
- Dashboard Training Template: use during Meeting 2.
- Team Rollout Template: use during Meeting 3.
- Weekly Coach Snapshot Template: use after launch.
- Stakeholder Check-In Template: use every two weeks with coach, sponsor, and key stakeholders.

8. Team Launch And Device Onboarding

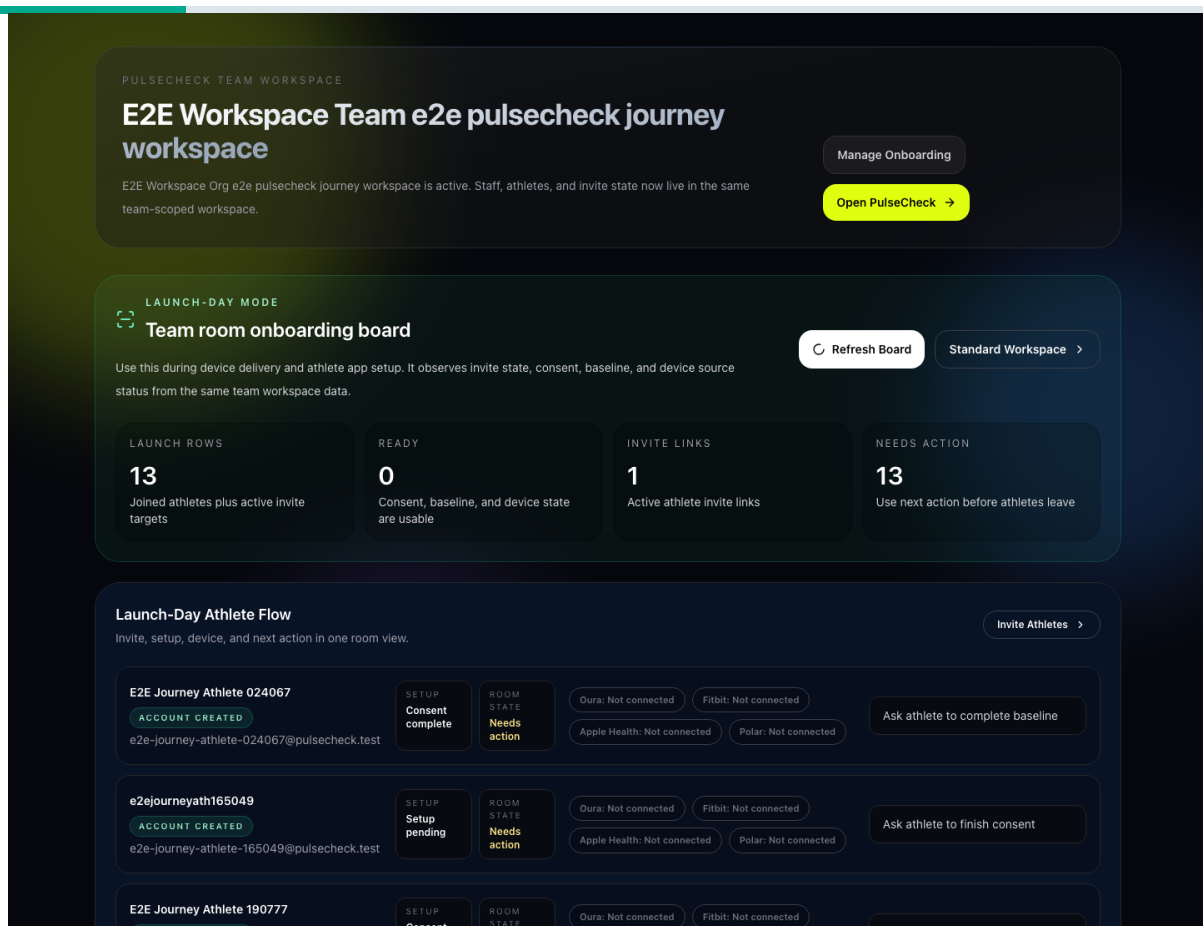

Screenshot 5 - Launch-Day Mode athlete onboarding board.

Open Launch-Day Mode from the tracker. Use the board to watch invite state, setup state, device status, and next action while the team is in the room.

Athlete launch flow

- Confirm athlete identity and team assignment.
- Install app or open invite path.
- Create account, join team, complete consent, and set notification permissions.
- Complete baseline or starting-point setup.
- Sync Oura, Fitbit, Apple Health, or Polar BLE where applicable.
- Complete first check-in.
- Complete the first protocol or simulation with PulseCheck staff present.
- Record unresolved device or setup issues before athletes leave.

9. Post-Launch Monitoring Cadence

The first two weeks after launch are where coaching habits are built. PulseCheck staff should keep a predictable rhythm so the coach knows when to expect interpretation, support, and stakeholder visibility.

Cadence	Owner	Purpose	Actions
Daily during first week	PulseCheck staff	Catch setup blockers early.	Review invite completion, device sync, check-ins, missing data, and support issues. Message the coach only when action is needed.
Weekly	PulseCheck owner	Coach snapshot and report rhythm.	Send a concise snapshot with team state, adherence coverage, meaningful changes, athlete support items, device gaps, and recommended coach actions.
Every two weeks	PulseCheck owner + stakeholders	Operating review.	Review adoption, coach questions, device health, report usefulness, athlete engagement, and unresolved blockers.
Monthly	PulseCheck leadership	Deployment health.	Review school-level outcomes, retention risk, product feedback, support load, and renewal or expansion signals.

Weekly coach snapshot structure

- Team state: one short summary of what changed.
- Coverage: what data is strong, missing, or stale.
- Athlete support: who may need a supportive conversation.
- Device gaps: what must be fixed before the next report.
- Coach action: the one or two actions that matter most this week.
- PulseCheck owner: named follow-up owner and due date.

10. Troubleshooting And Completion

Issue	Response
Coach cannot access dashboard	Confirm invite redemption, user email, team membership role, permission set, and roster visibility scope. Regenerate invite only after the membership path is checked.
Athlete joined wrong team	Remove incorrect membership, confirm roster source, resend the correct team invite, and document the correction in launch notes.
Device is missing or stale	Check source status, pairing state, battery, permission settings, and last sync time. Log hardware replacement only after software checks fail.
Coach over-interprets a single signal	Redirect the coach to trend, context, and coverage. Use the report reading order before recommending any athlete conversation.
Safety visibility item appears	Confirm ownership, document the route, and follow the school-approved protocol. PulseCheck staff should not improvise emergency handling.

Final admin review

- All tracker steps are Done or Needs help with owner, reason, and next date.
- Coach has completed guided dashboard training.
- Team rollout has occurred and device blockers are logged.
- Weekly coach snapshot cadence is scheduled.
- Every-two-weeks stakeholder check-in is scheduled.
- Support and escalation contacts are documented.
- First reviewed report has been delivered or its delivery date is scheduled.
